UTF/KEN/083/KEN
Terminal Report

FAO/UNILATERAL TRUST FUND

TECHNICAL ASSISTANCE FOR KENYA SMALL-SCALE IRRIGATION AND VALUE ADDITION PROJECT (TA-KSIVAP)

KENYA

PROJECT FINDINGS AND RECOMMENDATIONS

Report prepared for
the Government of Kenya
by
the Food and Agriculture Organization of the United Nations

FOOD AND AGRICULTURE ORGANIZATION OF THE UNITED NATIONS

Rome, 2023

The designations employed and the presentation of material in this information product do not imply the expression of any opinion whatsoever on the part of the Food and Agriculture Organization of the United Nations (FAO) concerning the legal or development status of any country, territory, city or area or of its authorities, or concerning the delimitation of its frontiers or boundaries. The mention of specific companies or products of manufacturers, whether or not these have been patented, does not imply that these have been endorsed or recommended by FAO in preference to others of a similar nature that are not mentioned. The views expressed in this information product are those of the author(s) and do not necessarily reflect the views or policies of FAO.

The Food and Agriculture Organization is greatly indebted to all those who assisted in the implementation of the project by providing information, advice and facilities.

TABLE OF CONTENTS

		Page
LIST OF ABBREVIATIONS		vii
A	OVERVIEW	1
A1	Project profile	1
A2	Financial data in USD	2
A3	Executive summary	2
B	RELEVANCE	4
C	ACHIEVEMENT OF R	

A. OVERVIEW

A.1 PROJECT PROFILE

Country	Kenya
Project Symbol	UTF/KEN/083/KEN
Project Title	Technical Assistance for Kenya Small-scale Irrigation and Value Addition Project (TA-KSIVAP)
Resource Partners	Global Agriculture and Food Security Programme (GAFSP) through Government of Kenya
Actual EOD	1 July 2016
Actual NTE	30 June 2021

A.2 FINANCIAL DATA in USD[1]

Latest Approved Budget	USD 1 200 000

A.3 EXECUTIVE SUMMARY

The agriculture sector in Kenya is critical to the national economy and has been identified as a priority area in national strategy and policies contributing to improving food security and nutrition. The Government, in line with Kenya Vision 2030, has launched a strategy to transform smallholder agriculture from its subsistence status into a modern, sustainable, commercially oriented and competitive sector. In support of this strategy, a GAFSP-supported project, "The Kenya Small-scale Irrigation and Value Addition Project-KSIVAP", was designed to enhance smallholders' agricultural competitiveness and food and nutrition security in eleven counties. The project required robust institutional, organizational and technical capacity at national and county levels to effectively deliver on its mandate and functions.

With the devolution of agriculture in 2010, the extension service, fundamentally at county level, had already presented critical capacity gaps, notably weak business, technical and managerial capacity, in providing adequate technical support for the commercialization of smallholder agriculture. In light of this, a targeted GAFSP-supported Technical Assistance (TA) project, was awarded to provide technical support and to complement KSIVf21(tec)6(hnica)6(l)-11( )] TJETQq0.000008867 0 595.08 842.185 Tm3.1412 Tfr4.981 3410051.71 529.51

Output 2 aimed to enhance the technical capacities and skills of extension officers and producer organizations (POs) to support development activities

Indications suggest that much of the support provided by the project will be sustainable and institutionalized into national and decentralized systems. Some target counties plan to incorporate new activities (marketing, business planning, agrinutrition) into their budget allocations and county integrated development plans (CIDPs). The project has stimulated the naming of nutritional focal points to coordinate agrinutrition interventions in counties, while the National NSAFS will serve as the principal nutrition-sensitive agriculture training package in the country. Furthermore, synergies have been established with other national programmes, including those supported by many development partners, who have expressed interest in the uptake of new materials (such as RuralInvest) promoted by the project.

B. RELEVANCE

The problem

Food and nutrition security remains a challenge in Kenya, despite significant opportunities to increase agricultural potential. The agriculture sector, dominated by smallholders, is characterized by low productivity as a result of low and unreliable rainfall, degraded land, the limited use of agricultural inputs and inadequate access to improved technology and markets, with incidences of food insecurity being more prevalent and more severe in the arid and semi-arid areas. The sector provides a livelihood (employment, income, and food security needs) to over 80 percent of the Kenyan population and contributes to improving nutrition through the production of safe, diverse and nutrient-dense foods.

To eradicate poverty and achieve food security and rural prosperity through the creation of wealth and employment, Kenya Vision 2030, launched in 2008, laid out the government strategy aimed at transforming smallholder agriculture from subsistence status into a modern, sustainable, commercially oriented and competitive sector by addressing a series of key challenges, including low production and productivity, constrained land use, inefficient markets and limited value addition. The Kenya Small-scale Irrigation and Value Addition Project . 842.04.05 Tm0 g0 G[(mar)5(7(produ)3(c)4(ti)-10 g0 GkTm0 .25 367.019 .M0 G[(smallhol)-4(de)4(rs)

The implementation of KSIVAP required strong institutional and technical capacity within public and private institutions, both at national and, fundamentally, at county levels, as the counties are responsible for extension service provision, following the adoption of a devolved system of government in Kenya in 2010. This led to the devolution of agriculture, including extension services, which became the full responsibility of county governments. The responsibility for policy development, planning and financing, and monitoring was expected to remain at national level.

The devolution and subsequent transition presented critical gaps, including weak business, technical and managerial capacity at national and county level, constraining

the capacities of public and private stakeholders to deliver efficient extension services and technical support at KSIVAP sites. Specifically, the TA project would strengthen the national and county coordination units in project management, including M&E, and complement their technical training in GAP, agrinutrition-sensitive interventions, agribusiness management and market development initiatives for improved smallholder commercialization and competitiveness, and increased food and nutrition security.

The strategy used to meet these objectives was to target and give priority to the PCU, CCUs and CPITs, as well as to POs, in terms of human and organizational capacity building to increase agricultural productivity and incomes, with a focus on agribusiness and market linkages, food security and nutrition-sensitive agriculture in the 11 counties. The strategy was initiated through a CNA of skills gaps at national, county and PO level that confirmed the technical gaps already identified during the devolution of agriculture. The primary strategies of intervention across the three main outputs and corresponding activities comprised TOT, technical workshops, technical guidance, on-the-job training, follow-up and backstopping, and the development of technical and training materials.

The TA project contributed directly to the implementation of the KSIVAP and therefore shares its impact (

Output 2: Capacity of county government technical staff and local private extension service providers to facilitate increased agricultural productivity and

Under Output 1, the TA project targeted 60 beneficiaries, both female and male, for the enhancement of project management and organizational skills, including five staff members from the PCU based at ministry headquarters, and 55 staff members (five from each county) from the CCUs based at the respective 11 county headquarters of Bomet, Kajiado, Kitui, Machakos, Makueni, Meru, Murang'a, Nyandarua, Nyeri, Tana River and Tharaka-Nithi. A total of 43 government staff beneficiaries received training in project management skills and knowhow. The orientation of training in terms of needs became flexible as a result of turnover in PCU staff, as new management ascribed to particular needs other than project management.

Under Output 2, the project targeted 33 county government technical officers with varied expertise to be trained as TOT trainers at county level, with the aim of complementing KSIVAP training and cascading that training to frontline extension staff and POs in the 17 project sites in the 11 counties. The technical officers would incorporate nutrition interventions into their day-to-day extension work, and develop skills and knowhow that would assist extension service providers to build strong community-based institutions able to maintain the infrastructure as well as manage the marketing of their products while infusing sustainability into project activities. However, "remedial" action was agreed on with KSIVAP and undertaken to reinforce the direct skills-building of producers when it became apparent that the TOT cascading approach was not reaching frontline extension staff and smallholder producers. This was caused by a lean extension service simultaneously allocated to other projects in the counties, and to delays in the flow of project funds to the counties, among other reasons. The PO leaders, including those of water users' associations, lead farmers and out-of-school youth with agricultural qualifications were consequently identified and trained as CBFs/CEVs in various thematic areas. The participants of this training totalled 140 (41 female and 99 male) including 49 (15 female and 34 male) frontline extension staff.

To further support agrinutrition interventions, 33 Community Health Volunteers

Under Output 3 the number of PCU M&E team members targeted to be mentored in the use of monitoring tools was five. However, following agreement with KSIVAP (May 2021), TA M&E support was considerably increased, notably in training on registration and activity monitoring, to cover a total of 108 participants (33 female and 75 male) including PCU, CPIT and other government key front-line staff.

As explained above, this TA project was in direct synergy with the AfDB-funded KSIVAP, as well as building on previous FAO-implemented projects of note

managerial and organizational skills, with special mention of M&E knowledge and skills, including the adoption and use of KoboCollect to report activities and beneficiaries reached (also linked with Output 3).

Activity 1.3.

using RuralInvest software in order to contribute to the enhanced development of off-farm opportunities and to diversify income generation and employment initiatives.

With regard to food and nutrition security, nutrition-sensitive agriculture and interventions were highlighted as competency gaps and tackled through two technical workshops, on nutrition-sensitive agriculture and food systems programming, respectively, to mainstream nutrition across sectors. These included a review workshop for the NSAFS training package held with the FNLTWG and another training workshop (in clusters) for 111 participants (46 female and 65 male). Two training events on agrinutrition for a total of 66 participants (49 female and 17 male) were supported, including the establishment of new space and water-efficient kitchen garden technologies, and fruit and vegetable preservation through drying to supplement the household food basket. Safe food handling and preparation, and family diet/meal planning taking into consideration the nutritional needs of different age cohorts within a household for improved household nutrition, in order to encourage the desire for healthy diets, were also covered by the training.

On increasing agricultural productivity, the concept of GAP was clarified in various training events for the PCU, county extension officers and CBFs, with an emphasis on the guiding principles of GAP and the role GAP plays in environmental conservation, the social wellbeing of communities, food safety and improved productivity. The principles of CA, such as minimum tillage, crop rotation and ensuring soil cover, were also promoted, contributing to increasing productivity and efficiency, including labour-saving, and the climate-resilience of agrifood systems. During agribusiness and marketing development training for county agribusiness development officers, guidelines on GAP were covered as a module for a total of 28 participants (10 female and 18 male). In addition, during capacity building for subcounty frontline extension service providers and CBFs, training in GAP, CA

The development of the M&E framework and data collection tools and such corresponding activities as coaching on how to use the tools have led to enhanced knowledge of M&E and higher capacities for implementation. The PCU is now championing the use of the M&E system in another AfDB-supported project under its jurisdiction.

Activity 3.2. Support monitoring of KSIVAP's CD activities and provide technical backstopping at county level

This activity was delivered. The project completed two core products: the development of an agrinutrition reference manual, a user-friendly, practical resource tool to be used by frontline extension providers and community facilitators on a range of agrinutrition themes (production, hygiene, processing, preservation, utilization, etc.); and the drafting of the National NSAFS training package. The project facilitated the development of the NASFS through collaboration with the nutrition technical network group partnership. The working group is committed to continuing support to its final packaging, dissemination, and uptake. Members include WFP, GiZ, and NGOs such as World Vision.

Activity 3.3. Hold county stakeholders' implementation progress review meetings

This activity was delivered.

Beneficiaries

The project engaged government stakeholders at national and county level, and frontline producers from the 17 project sites, reaching a total of 658 (278 female and 380 male) comprising government staff (534 [231 female and 303 male]), PO leaders (51 [16 female and 35 male]), CHVs (33 [21 female and 12 male) and out-of-school youth (40 [10 female and 30 male]). See Table below.

Table 1: Beneficiaries

Participants	Planned number	Actual number		
	Total	Total	Female	Male
Output 1				
PCU staff (Ministry				

With regard to enhanced managerial capacity, the PCU and most counties' desk officers have demonstrated the capacity to use the M&E digitized data collection and reporting tools (see Photo 1 below) and are eager to continue. This has been an important contribution to improving project management and monitoring project progress.

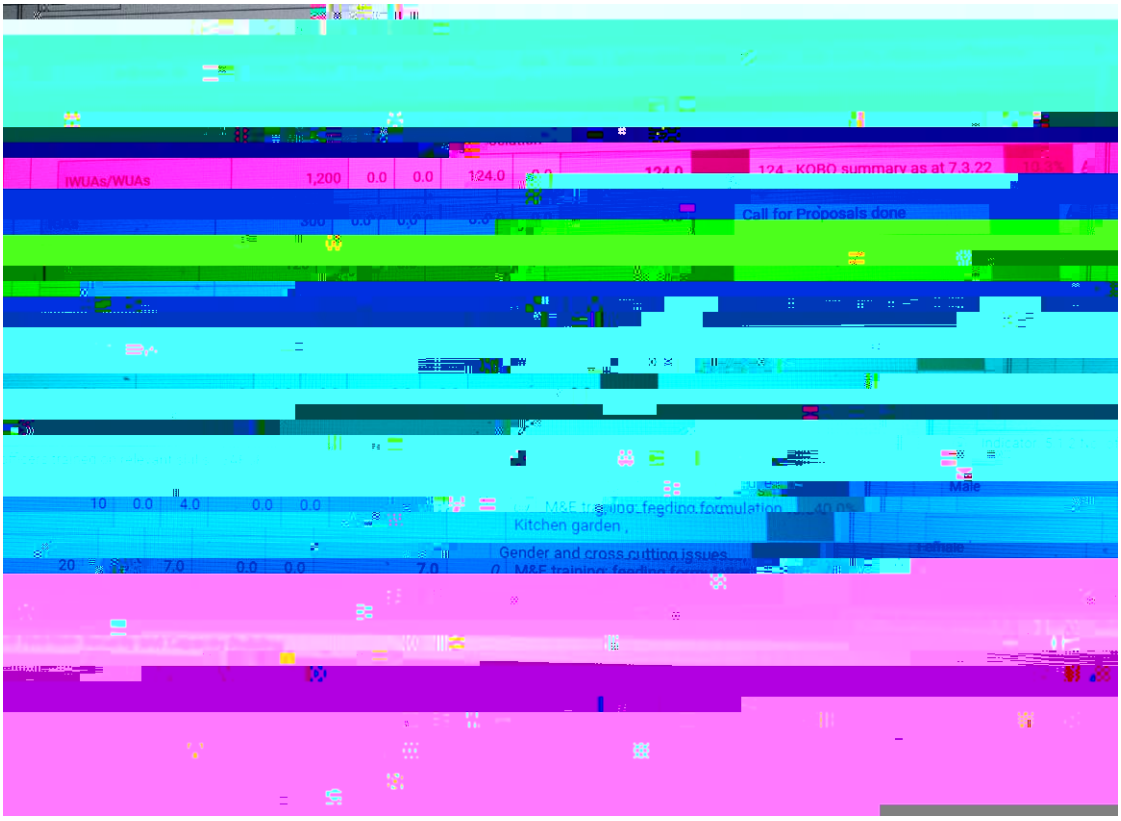

Photo 1: M&E tool screenshot from one of the Counties, Nyeri. (Credit: ©FAO Kenya).

With regard to enhanced technical capacity, most

Photo 2: Trainee presents BMC during NARIGP training conducted by TA Agribusiness beneficiary/TOT from Makueni. (Credit: ©FAO Kenya).

D. IMPLEMENTATION OF WORK PLAN AND BUDGET

Work plan and budget

Project activities were well planned but risks initially identified in the Project Document posed challenges for their timely implementation. These included high staff turnover in the PCU, which led to deviations in planning and the non-synchronization of schedules between the two projects. Bureaucratic delays in the flow of government funds to KSIVAP led to the delayed implementation of training activities as the investment project could not facilitate its implementing teams to participate in planned training. The investment project was supposed to procure the training venue and provide

Risk management

A project design lapse affected the investment project start-off, leading to the delayed implementation of the TA project and missed activities, as highlighted by the MTR in July 2019. In addition, delays in KSIVAP implementation were caused by the decentralized government structure and associated unforeseen challenges of devolution transition in governance and institutional changes. Further delays were caused by the priority given to infrastructure development by the investment project, effecting the TA start-off. An agreed matrix of actions and recommendations with timelines was subsequently developed during the MTR for accelerated implementation. Minimal activities however took place owing to the non-synchronization of activities, and weak collaboration and coordination between the TA

Visibility

The TA task leader participated in initial public inception visits to the counties and an initial sensitization workshop informing main stakeholders of the role of the TA. Training workshops, specifically in nutrition training, were officially opened by senior government officers. The task leader took advantage of other meetings held with the PCU and other stakeholders, including AfDB supervision missions, GAFSP coordinating unit missions and the joint MTR, to provide updates on the project. Results were also disseminated through the technical backstopping mission held in 2021 to all 11 counties, during which county executive committee members, including agriculture chief officers and county directors of agriculture, were consulted, and the technical backstopping mission to Makueni and Nyeri in May 2022 at which the respective local authorities were present. These provided an opportunity not only to discuss successes with county leadership and stakeholders, but also to emphasize the importance of successes and the need to carry forward planned project activities.

A stakeholder review meeting held in June 2022 discussed project results, achievements, issues and challenges of implementation, while making collective decisions on how to improve KSIVAP project performance in the remaining period of implementation.

The kitchen garden training support provided by TA-KSIVAP is a relatively uniform “model” tool that can be easily replicated for uptake by counties and below. A central demonstration plot developed by KSIVAP and others, including the TA project, at MOALF&C Headquarters

E. SUSTAINABILITY

a. Capacity development

The project made a significant investment to strengthen the institutional, organizational and human capacity of government staff at national and county levels to implement the KSIVAP. Technical officers at national and county level, as well as CBFs/CEVs, have acquired improved knowledge and capacity for enhanced technical performance in business, nutrition practices, production, contributing to reducing hunger, improving nutrition, reducing poverty and increasing incomes in the project sites and beyond. Frontline trainers have the requisite capacity to provide training related to improved institutional and technical capacity to upscale and replicate inclusive business and market linkage models, and provide complementary support to increase value addition and competitiveness. The technical workshop to incorporate and mainstream nutrition-sensitive agriculture in programming built momentum for the counties to integrate nutrition in their CIDPs and provide complementary support to NSAFS while fulfilling their mandates; some counties have already demonstrated commitment. The RuralInvest training has stimulated high interest, including among partners, suggesting promising scale-up potential for the method and tool.

All county staff members are subject matter specialists or extension agents involved in such government agricultural/livestock projects as the Drought Resilience and Sustainable Livelihoods Project, NARIGP, KCSAP, ASDSP, ABDP and the Upper Tana Catchment Natural Resources Management Project (IFAD) in their respective counties. This gives them leverage to use the knowledge and skills acquired through the project, resulting in further scale-up in, *inter alia*, nutrition, agribusiness and market development, GAP and participatory M&E.

Strengthening the capacity of county extension agents and CBFs/CEVs promotes the sustainability of knowledge and skills gained through the TA among farming communities. At the time this report was written, Makueni County had just recruited 230 CEVs, adding to the existing extension service. As eight of these (all youths) attended CBF/CEV training, this should further disseminate the transferred TA knowledge.

b. Gender equality

Although the TA project did not have gender equality as one of its main objectives, it addressed the issue in a systematic manner. Female trainers and trainees were mobilized alongside males and received the same training and participation in technical and business management skills. By default, CD activities enhanced the participating women’s technical,

business and entrepreneurial skills. The project promoted women-friendly and labour-saving agricultural technologies and practices such as the use of energy-saving fireless cookers, minimum tillage in CA and kitchen gardening, as well as access to markets and opportunities for value addition and cottage industry development, and the promotion of inclusive value chains and business models. The use of CBFs/CEVs/CHVs enhances proximity, allowing more females to become involved in farmer-farmer extension without having to travel far from home and allowing them to learn as they train and receive coaching and mentoring by the extension staff.

c. Environmental sustainability

As the project is a capacity-building project, there were no environmental risks that might have threatened the sustainability of outcomes, and this parameter is therefore

kitchen gardens for a fee and looking into using RuralInvest to formulate business plans for projects and entrepreneurs for a fee. The TA project provided training in CA, especially in minimum tillage and cover cropping, which has been shown to reduce drudgery and excessive hours of work, allowing time to engage in other productive activities, while GAP and IPM support measures for ecological and food production sustainability and improved services for marketing through promoting tools and techniques, thus improving labour conditions in rural areas.

e. Technological sustainability

Most training targeted 'learning by doing' and most technological knowhow acquired is sustainable, with much of it leveraging local products. There is high potential for sustainability and institutionalization of the competencies and technologies supported through the CD interventions of the project, mainly because the training reached government officers at both national and county levels, and also out-of-school youth, frontline PO leaders and lead farmers living in the farming communities, and farmers themselves. A priority emphasized in all training was that the trainees involved in the various project CD activities would share the technological knowledge, skills and information acquired with others.

f. Economic sustainability

County extension staff members are permanent and pensionable employees, paid by the county, and will incorporate the knowledge and skills gained in their regular extension services beyond the project. The CBFs/CEVs are community members living among the farming communities and will by default pass on the knowledge and skills gained even in the absence of external funding. The CD attained, particularly in terms of strengthening business and agro-entrepreneurial skills, including value-addition technologies, will contribute to the growth of value addition and cottage industries, micro and small enterprises, income diversification and off-farm employment, business and market opportunities along the agricultural value chain, all of which will translate into inclusive rural transformation and economic development. RuralInvest will be used to design agricultural-related investment proposals for activities to increase incomes.

Technical capacity to support the business and technical training of producers at project sites will improve producers' business planning, management and technical skills, enabling them to supply sufficient high-quality produce in a timely manner and leading to improved incomes.

F. LESSONS LEARNED

LESSONS LEARNED – elements of success

The initial CNA, also serving as a baseline for institutional strengthening and CD projects, proved to be both useful and important. Most CD interventions and activities with the PCU, CCUs and CPITs in specific managerial, technical and business skills were highly relevant to the needs of the target counties.

The project provided a platform for knowledge and experience-sharing. With locally held workshops, attendance and participation were frequently 100 percent.

Conducting workshops and training jointly with the PCU, CCU and CPITs was an efficient way of facilitating the cross-fertilization of ideas. At the same time, adopting the farmer-to-farmer approach,

A female farmer group member used the income generated by vegetable sales from her kitchen garden to scale up and commercialize her poultry enterprise. She had started with few poultry but now reported to have 100 chickens, used for both household consumption and sales. She felt more “empowered” and “respected” particularly within the household: “Before I was living like a beggar. I am now selling; I bring home food myself. And I am now producing, I am contributing to the household income.”

Appendix 1

LOGFRAME MATRIX ACHIEVEMENT OF INDICATORS

Results Chain	Indicators				If not achieved, explain why	If applicable/ follow-up action to be taken
	Indicators	Baseline	End target (*expected value at project completion*)	Achieved		
Impact[2]	Contribute to reduction of rural poverty and food insecurity in the eleven counties					

Results Chain	Indicators				If not achieved, explain why	If applicable/ follow-up action to be taken
	Indicators	Baseline	End target (*expected value at project completion*)	Achieved		
Output 2 Capacity of county government technical staitadW*3(						

Appendix 2

PROJECT STAFF

Function	Dates of Service	
	Starting Date	Concluding Date

Appendix 3

TRAINING AND STUDY TOURS

No. of participants	Training and Study Tours	Place	Date
1 (female)	GAFSP knowledge forum	Rome	30 May 2017- 1 June 2017
20 (6 female and 14 male)	Principles and practices of project management	Thika	30 October 2017- 3 November 2017
23 (8 female and 15 male)	Fundamentals of M&E	Thika	26-29 March 2018

Appendix 4

MAJOR ITEMS OF EQUIPMENT PROVIDED

Quantity	**Item**	**Cost (USD)**
1	Projector, Epson 2155W 5000, plus Elite Screen	3 619
1	Computer, laptop, EliteBook 830 G6	1 484
